


EXCAVATION – GAL(07)

START DATE:1/01/2025

END DATE: 1/01/2025

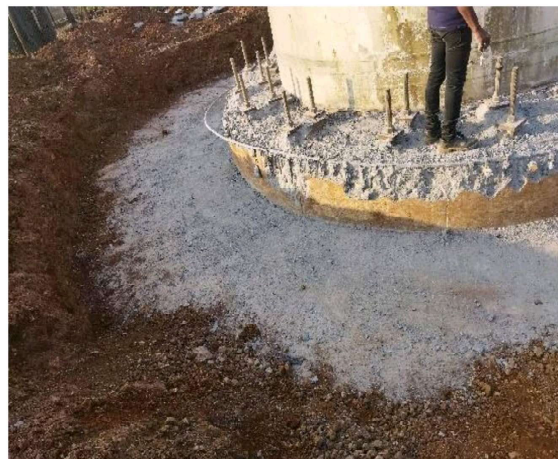

BREAKING OF EXISTING CONCRETE- GAL(07)

START DATE: 20/01/2025 END DATE:2/03/2025



CLEANING OF EXISTING REINFORCEMENT AND APPLICATION OF ANTI-CORROSIVE ZINC RICH COATING- GAL(07)

START DATE- 22/03/2025 END DATE:29/03/2025



CUTTING OF EXISTING 36 NO.S GEWI STUD- GAL(07)

START DATE:20/03/2025 END DATE: 22/03/2025



FIXING OF STUDS – GAL(07)

START DATE:08/04/2025 END DATE: 08/04/2025




PRESSURE GROUTING USING CONBEXTRA EP-10 - GAL(07)

START DATE:04/03/2025 END DATE: 10/03/2025



DRILLING OF HOLES AND FIXING PF STUDS(M36) USING FOSROC CHEMICAL(LOKFIX) – GAL(07)

START DATE:21/03/2025 END DATE: 10/04/2025

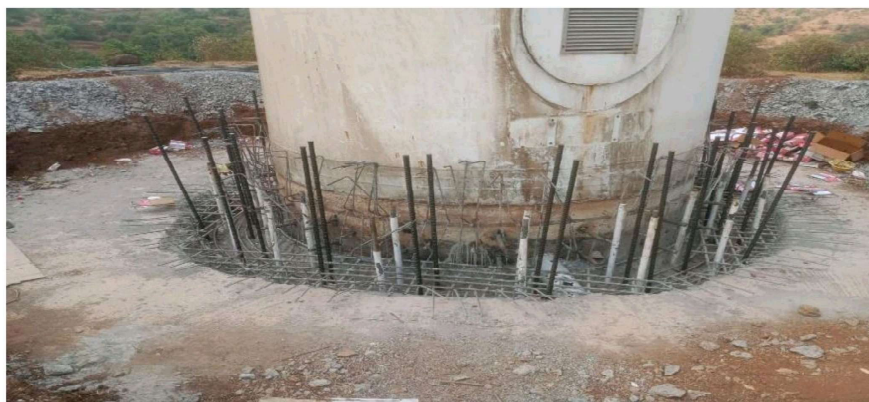

STEEL WORK OUTSIDE FOR PEDESTAL(GAL-07)

START DATE-22/05/2025 END DATE-25/05/2025



SHUTTERING AND CONCRETE OF PEDESTAL OUTSIDE(GAL-07)

START DATE-29/05/2025 END DATE-30/05/2025



CURING(GAL-07)


START DATE- 02/06/2025 END DATE- 29/06/2025



CHIPPING WORK INSIDE WTG(GAL-07)

START DATE- 06/06/2025

END DATE- 09/06/2025

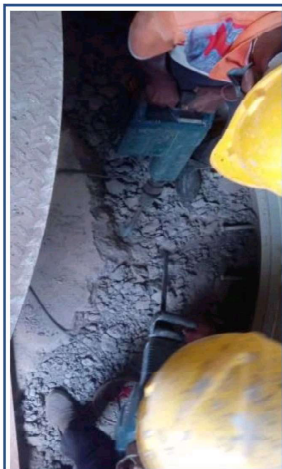

INJECTION GROUTING INSIDE(GAL-07)

START DATE-13/06/2025

END DATE- 17/06/2025





ANCHOR STUD FIXING INSIDE(GAL-07)

START DATE-18/06/2025 END DATE- 24/06/2025



STEEL WORK, SHUTTERING & CONCRETE OF PEDESTAL INSIDE WTG(GAL-07)

START DATE-26/06/2025 END DATE- 04/07/2025

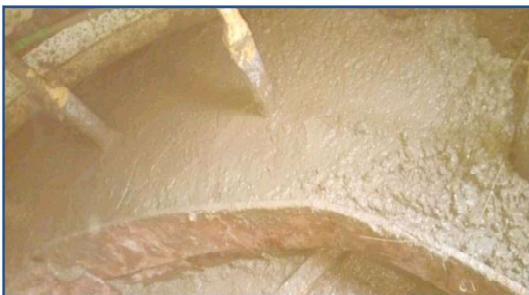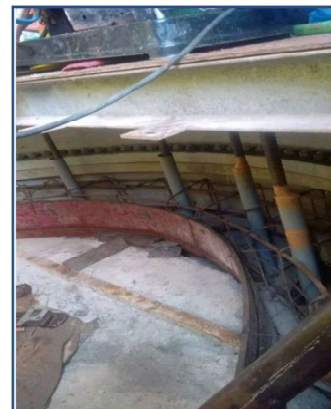

BACKFILLING(GAL-07)

START DATE- 07/07/2025 END DATE- 07/07/2025



GROUTING INSIDE AND OUTSIDE

WTG(GAL-07)

START DATE- 01/07/2025 END DATE- 03/07/2025



WATER PROOFING GAL - 07

